Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
Milestones				
00010	Notice to Proceed	0	14APR08A	
00030	Foundation Complete	0		05JUN08
00020	Project Dry In	0		13JUN08
00050	Rough-Ins Complete	0		19JUN08
00040	Drywall Complete	0		30JUN08
00070	Project Turnover	0		14AUG08
Deliveries & Selections				
00270	Windows	40	13MAR08A	11JUN08
00090	Deliver SIP Panels	40	17MAR08A	21MAY08A
00080	Deliver Floor Framing	0	30APR08A	
00100	Trusses	10	16MAY08A	02JUN08A
00420	Siding and Trim	14	26MAY08A	17JUN08
00110	Metal Roofing	7	09JUN08A	16JUN08
00130	Deliver Fixtures	21	17JUN08	15JUL08
00140	Sel/Del Wood Floor	14	17JUN08	04JUL08
00440	Cabinets & Vanities	14	17JUN08	04JUL08
00120	Deliver Drywall	0	20JUN08	
00150	Deliver Tile	10	26JUN08	09JUL08
00160	Deliver Carpet	14	30JUN08	17JUL08
00530	Acclimate Wood Floor	7	07JUL08	15JUL08
00280	Interior Trim	10	11JUL08	24JUL08
Construction				
00170	Excavation	2	24APR08A	24APR08A
00180	FRP Footings and Stemwall	3	28APR08A	02MAY08A
00430	FRP Garage Footings and	3	30APR08A	02MAY08A
00610	Set Floor Beams	1	05MAY08A	05MAY08A
00200	Floor Framing and Sheathing	2	07MAY08A	08MAY08A
00620	Insulate and Waterproof	3	07MAY08A	09MAY08A
00210	Backfill Foundation	2	12MAY08A	23MAY08A
00220	Erect SIP Panels	3	21MAY08A	28MAY08A
00460	Interior Framing	3	23MAY08A	29MAY08A
00410	Garage Radiant Tubing	1	25MAY08A	26MAY08A
00320	FRP Ext Decks	2	27MAY08A	28MAY08A
00310	Set Deck Posts & Beams	2	30MAY08A	02JUN08A
00230	Truss Installation	3	02JUN08A	04JUN08A
00240	Roof Overframing	2	04JUN08A	06JUN08
00250	Roof Sheathing	2	05JUN08A	09JUN08
00190	FRP Garage Slab	3	06JUN08A	05JUN08

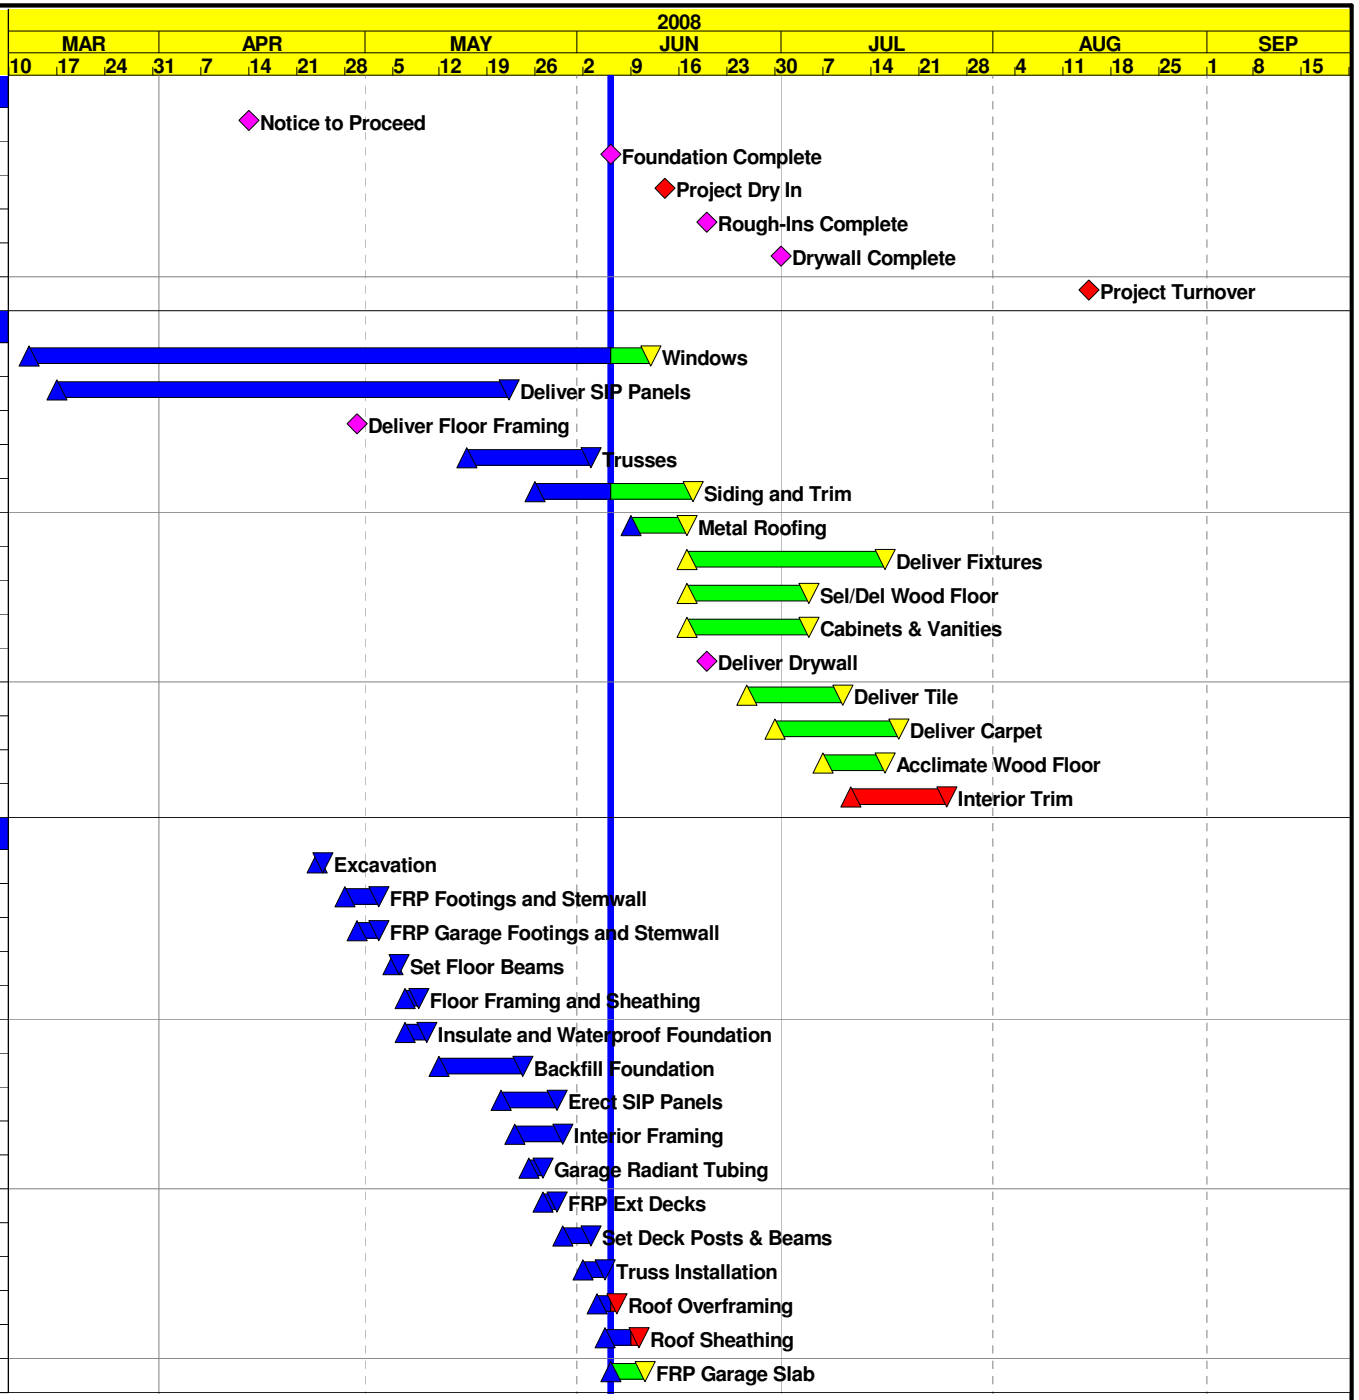

Start Date	11FEB08
Finish Date	14AUG08
Data Date	06JUN08
Run Date	04SEP08 14:19

© Primavera Systems, Inc.

NEWP

WIT Construction Co.

0712-008 Newport Residence

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
00580	Ext Final Grades	2	06JUN08	09JUN08
00390	Radiant Tubing	2	09JUN08	10JUN08
00300	Metal Roofing	2	10JUN08	11JUN08
00370	Mech RI	4	11JUN08	16JUN08
00260	Windows and Ext Doors	2	12JUN08	13JUN08
00380	Solar Panel Installation	2	12JUN08	13JUN08
00350	Plumbing RI	4	16JUN08	19JUN08
00360	Elec RI	3	16JUN08	18JUN08
00290	Siding, Soffit, and Trim	8	16JUN08	25JUN08
00450	Drywall	7	20JUN08	30JUN08
00520	Insulate Ceiling	1	01JUL08	01JUL08
00470	Paint	3	02JUL08	04JUL08
00400	Cabinets & Vanities	3	07JUL08	09JUL08
00480	Tile Flooring	4	10JUL08	15JUL08
00490	Wood Flooring	2	16JUL08	17JUL08
00550	Plumbing Fixtures	2	16JUL08	17JUL08
00500	Carpet	3	18JUL08	22JUL08
00510	Interior Doors	2	23JUL08	24JUL08
00570	Elec Fixtures and Trim	3	23JUL08	25JUL08
00560	Mech Trim	1	23JUL08	23JUL08
00540	Interior Trim	5	25JUL08	31JUL08
00590	WIT Punchlist	5	01AUG08	07AUG08
00600	Owner Punchlist	5	08AUG08	14AUG08

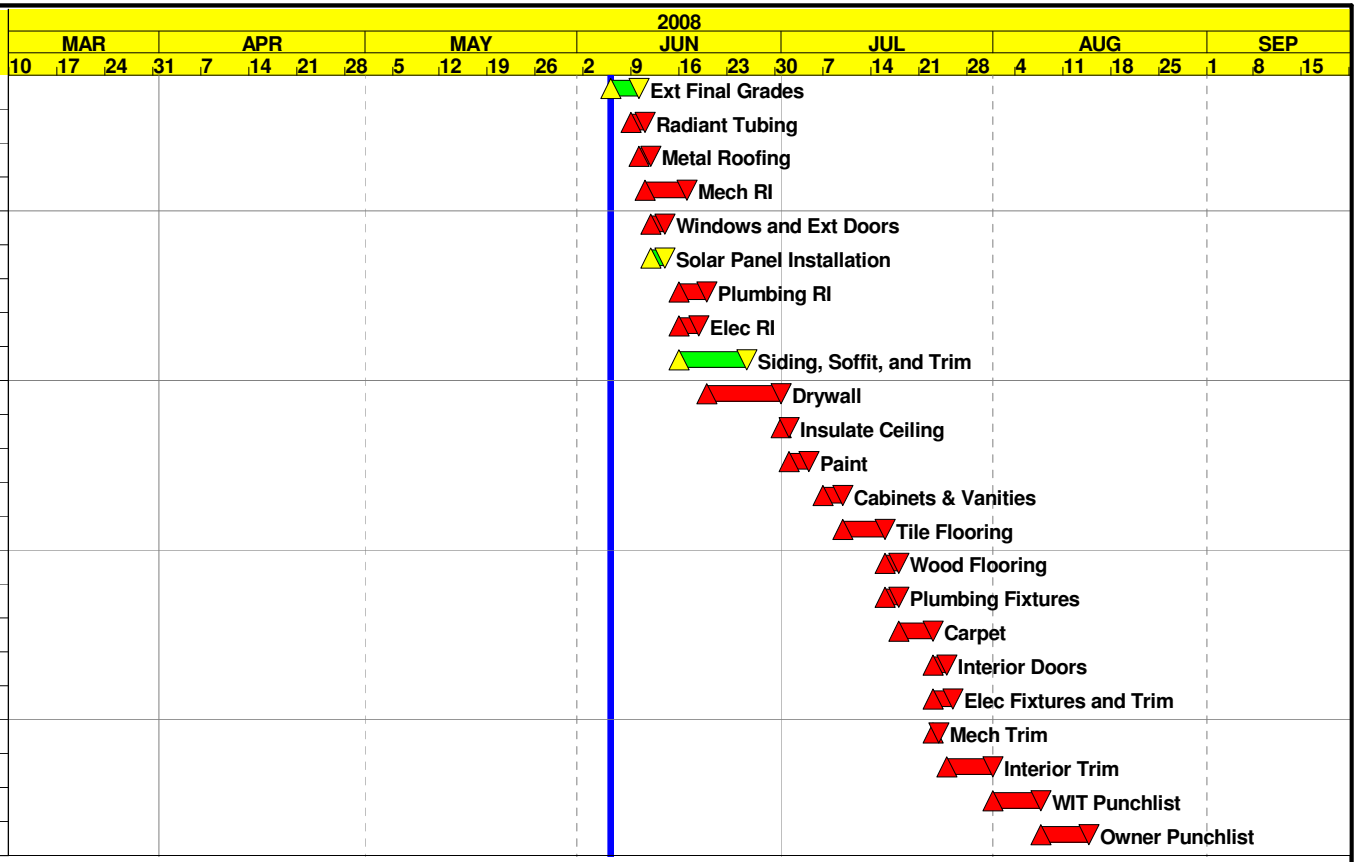

Start Date	11FEB08
Finish Date	14AUG08
Data Date	06JUN08
Run Date	04SEP08 14:19

© Primavera Systems, Inc.

NEWP

WIT Construction Co.

0712-008 Newport Residence

Date	Revision	Checked	Approved
